




2019 Road Recycling Program

Updated on September 12, 2019

- Road Paving Complete
- Paving in Progress
- Base Complete
- Recycling In Progress
- 2019 Tentatively Scheduled
- ON HOLD (Contractor Strike)

- Roads**
- Freeway
 - Routes
 - Primary
 - Local Paved
 - Local Gravel
 - Private Drive

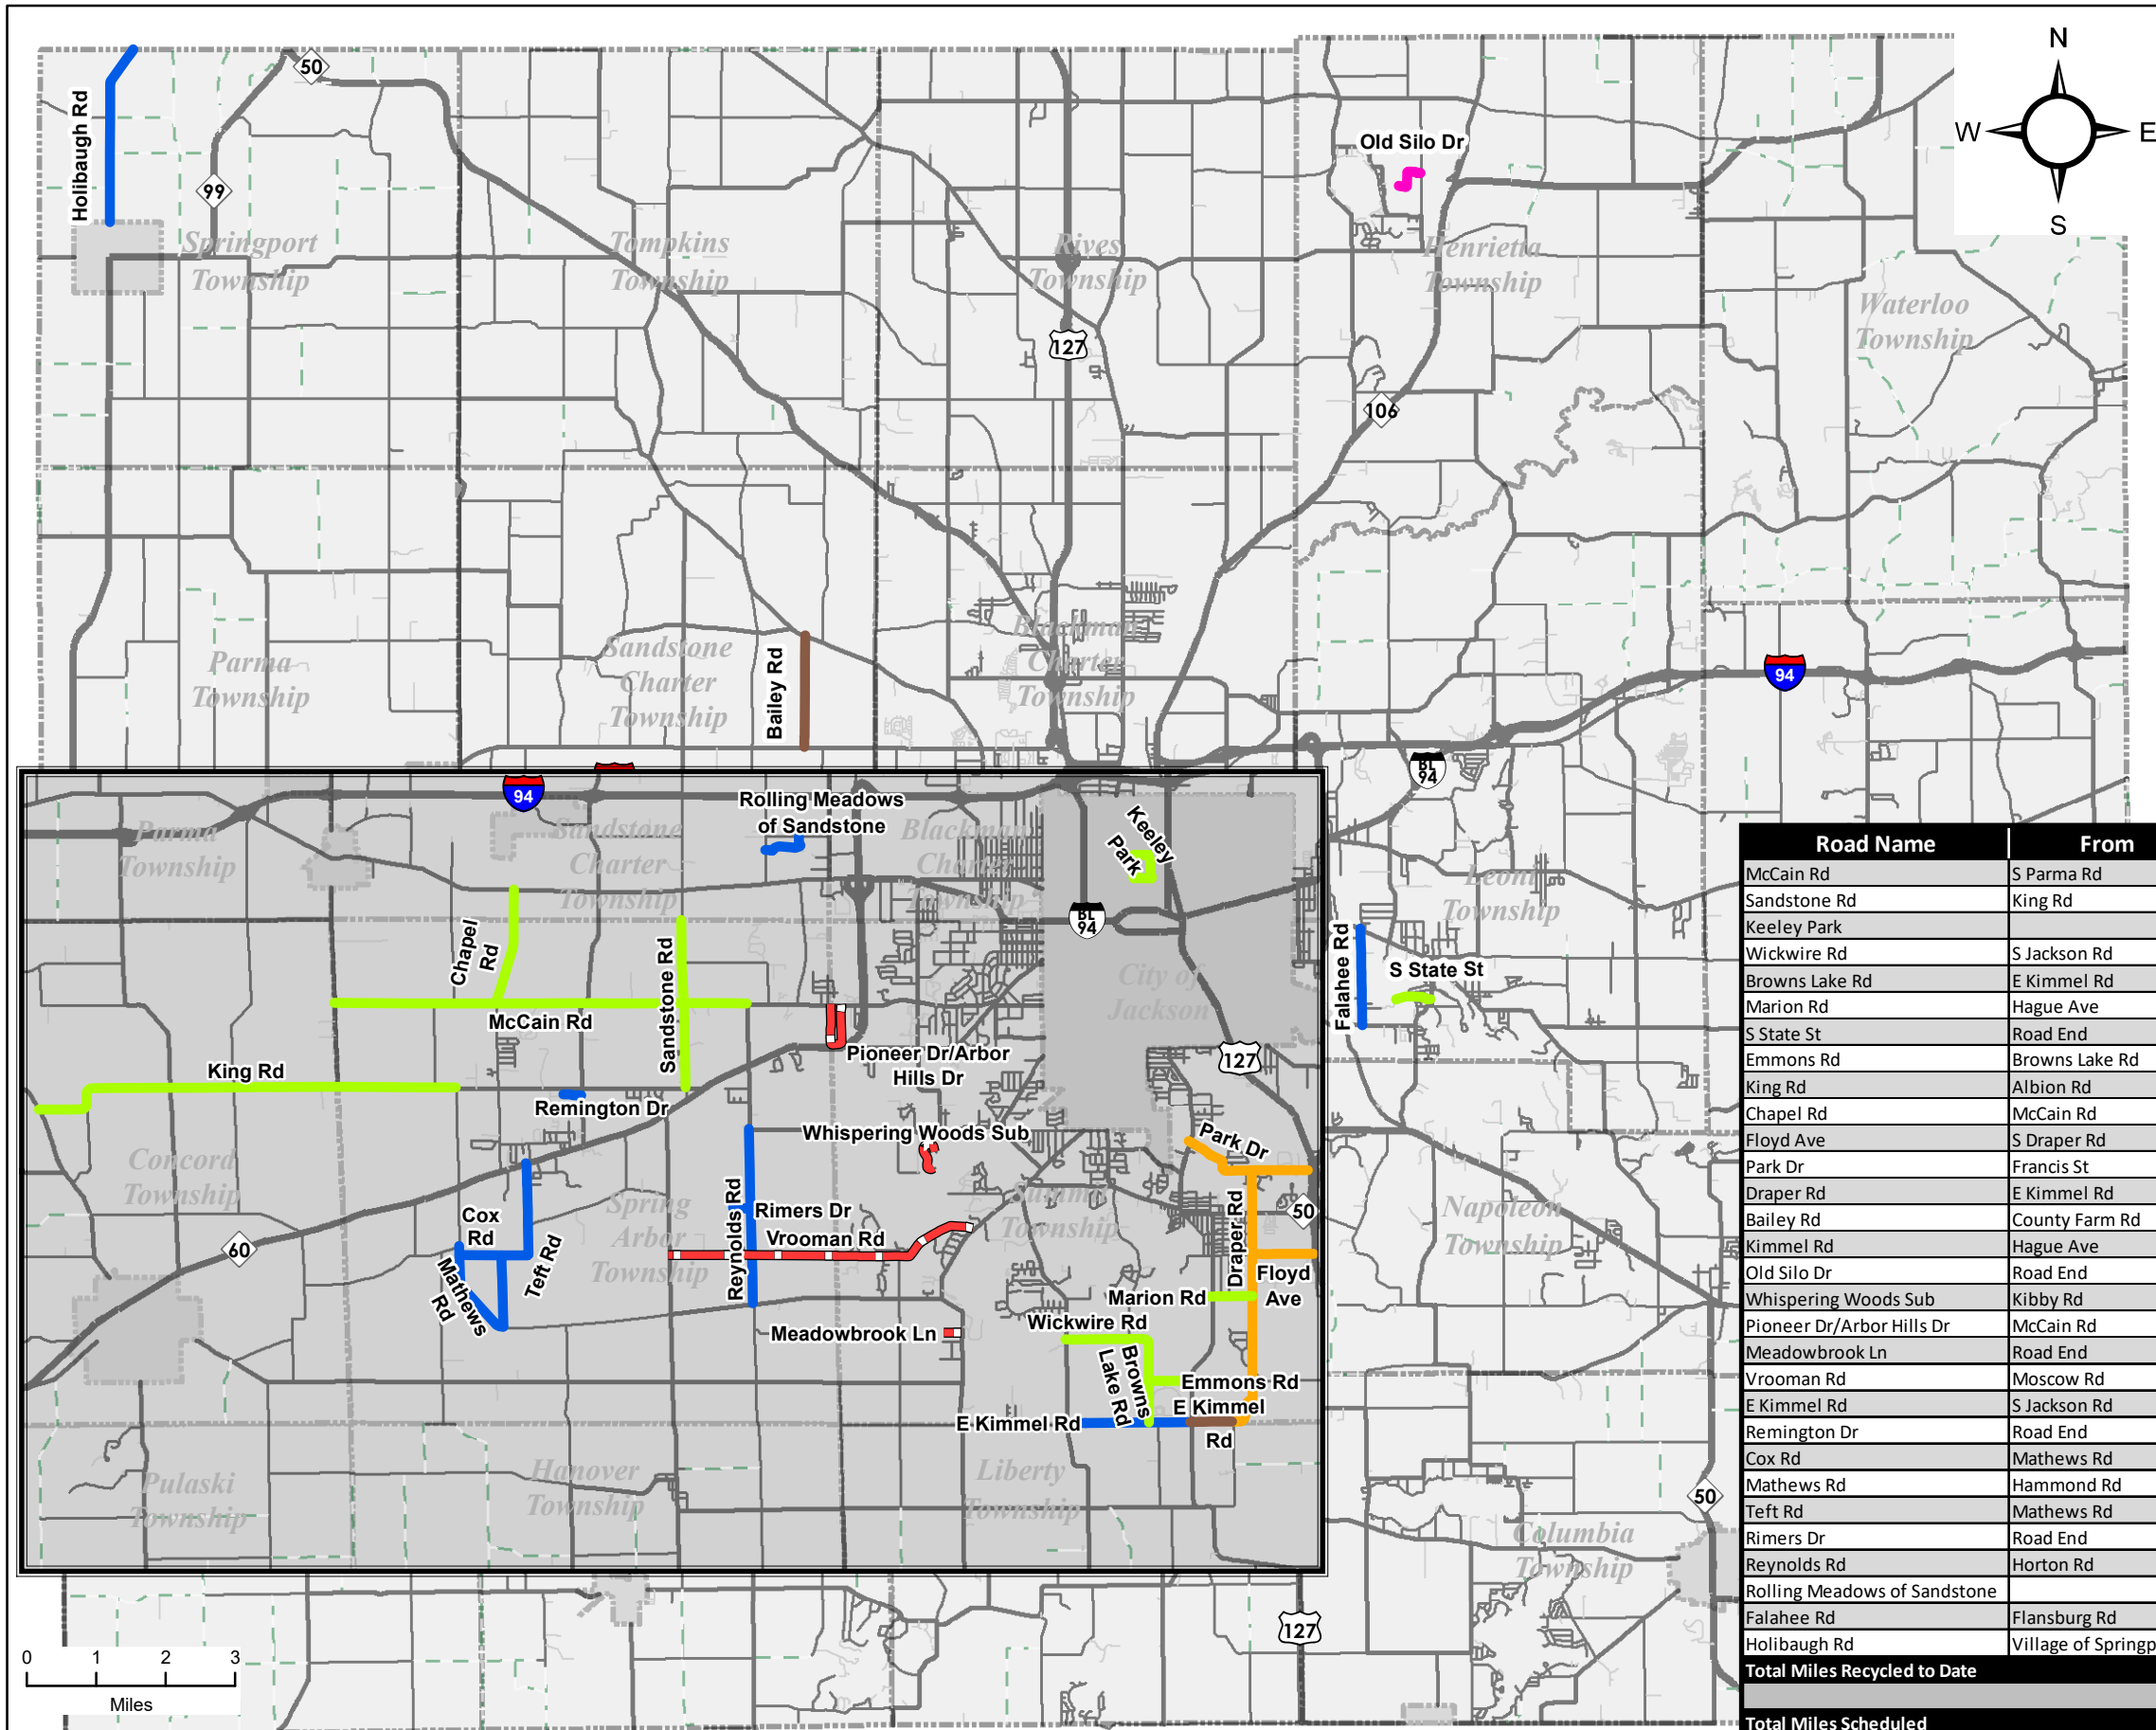

Road Name	From	To	Estimated Start Date	Estimated Length (miles)
McCain Rd	S Parma Rd	Reynolds Rd	Road Paving Complete	4.95
Sandstone Rd	King Rd	Township Line	Road Paving Complete	2
Keeley Park			Road Paving Complete	1.3
Wickwire Rd	S Jackson Rd	Browns Lake Rd	Road Paving Complete	0.98
Browns Lake Rd	E Kimmel Rd	Wickwire Rd	Road Paving Complete	1.23
Marion Rd	Hague Ave	S Draper Rd	Road Paving Complete	0.5
S State St	Road End	Fifth St	Road Paving Complete	0.5
Emmons Rd	Browns Lake Rd	Hague Ave	Road Paving Complete	0.5
King Rd	Albion Rd	Mathews Rd	Road Paving Complete	5.2
Chapel Rd	McCain Rd	E Michigan Ave	Road Paving Complete	1.04
Floyd Ave	S Draper Rd	S Meridian Rd (US-127)	Paving In Progress	0.75
Park Dr	Francis St	Oaklane Rd	Paving In Progress	1.6
Draper Rd	E Kimmel Rd	Park Dr	Paving In Progress	2.98
Bailey Rd	County Farm Rd	Springport Rd	Base Complete	1.61
Kimmel Rd	Hague Ave	Draper	Base Complete	0.5
Old Silo Dr	Road End	Hankerd Rd	Recycling In Progress	0.52
Whispering Woods Sub	Kibby Rd	Road End	HOLD	0.69
Pioneer Dr/Arbor Hills Dr	McCain Rd	Arbor Hills Rd	HOLD	1.42
Meadowbrook Ln	Road End	Springbrook Rd	HOLD	0.21
Vrooman Rd	Moscow Rd	Horton Rd	HOLD	3.79
E Kimmel Rd	S Jackson Rd	Hague Ave	9/16/2019	1.5
Remington Dr	Road End	S Dearing Rd	9/23/2019	0.22
Cox Rd	Mathews Rd	Teft Rd	9/25/2019	0.51
Mathews Rd	Hammond Rd	Teft Rd	9/27/2019	1.11
Teft Rd	Mathews Rd	M-60	10/2/2019	2.28
Rimers Dr	Road End	Reynolds Rd	10/8/2019	0.4
Reynolds Rd	Horton Rd	Kibby Rd	10/14/2019	2.09
Rolling Meadows of Sandstone			Tentative	0.48
Falahee Rd	Flansburg Rd	Page Ave	Tentative	1.39
Holibaugh Rd	Village of Springport	N County In	Tentative	2.59
Total Miles Recycled to Date				25.6
Total Miles Scheduled				44.8

DISCLAIMER: Maps are drawn as accurately as possible. They are intended to be a visual aid for road construction and related projects. They are subject to change based on new information and do not take the place of a formal contract.

Note: This schedule is tentative. Factors can and often do arise, such as weather and scheduling conflicts, that cause project timelines to change. This exhibit will be updated accordingly.

Source: Jackson County Department of Transportation
